

Cuyamaca College Facilities Update

April, 2019



Campus Projects

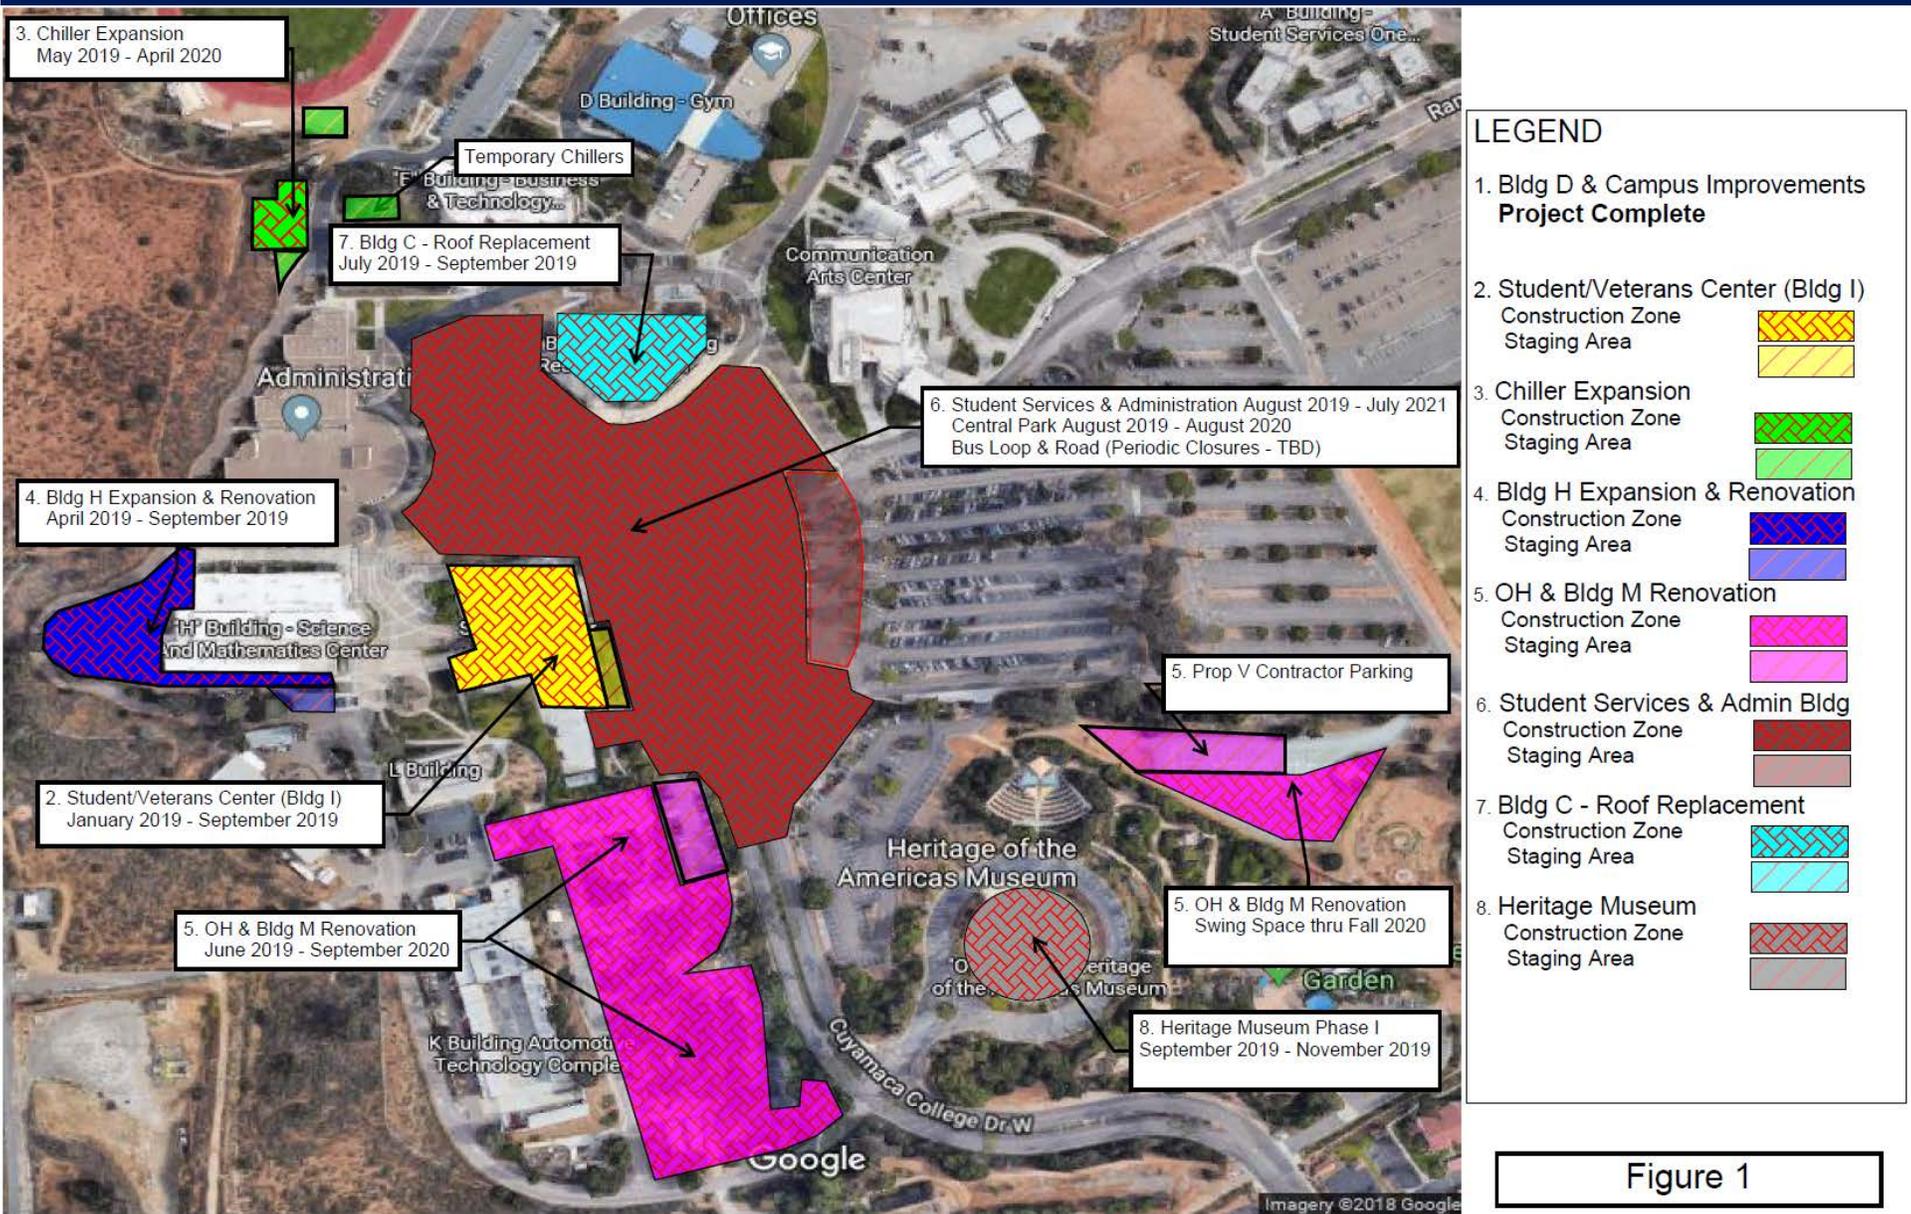


Figure 1

Student Services & Administration Building

Funding:

- Prop V

Design:

- SSAB Construction Drawings complete; Central Park by late February

DSA Submittal

- November 2018 (SSAB); March 2019 (Central Park)

Bidding/Award:

- May – July 2019

Construction:

- Anticipated Fall 2019-2021

Status:

- Finalize Central Park landscaping design



Building I – Student/Veterans Center Renovation

Funding:

- Prop V

Design:

- Complete

Bidding/Award:

- Complete

DSA Submittal


- Approved

Construction:

- January 2019- September 2019

Status:

- Barnes & Noble-work will begin Spring break 2019
- Coyote Grill / C-Store / RR / CR work will start after Commencement – will re-open by August 1st
- Job Placement & Career Center work will start after C-Store moves to new spaces and complete in September

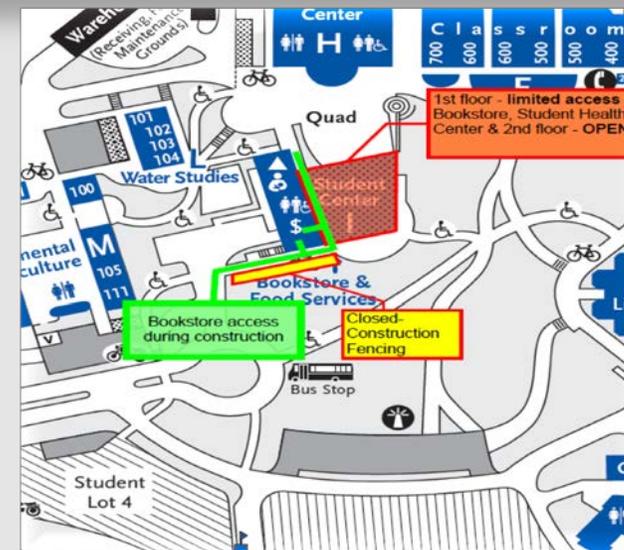

Ornamental Horticulture / M Remodel

Funding:

- Prop V

Design:

- Complete

DSA Submittal:

- Approved

Bidding/Award:

- Bids opened February 7th

Construction:

- March 2019-August 2020

Status:

- Swing Space work at gravel parking lot continues (multiple weather impacts); move anticipated week of February 18



Building H (Title III) – Biology & Chemistry Labs

Funding:

- Title III Grant/Prop V

Design:

- Complete

DSA

- Infrastructure approved

Bidding/Award:


- January 2019-March 2019

Construction:

- April 2019-August 2019

Status:

- Bid opening February 2019

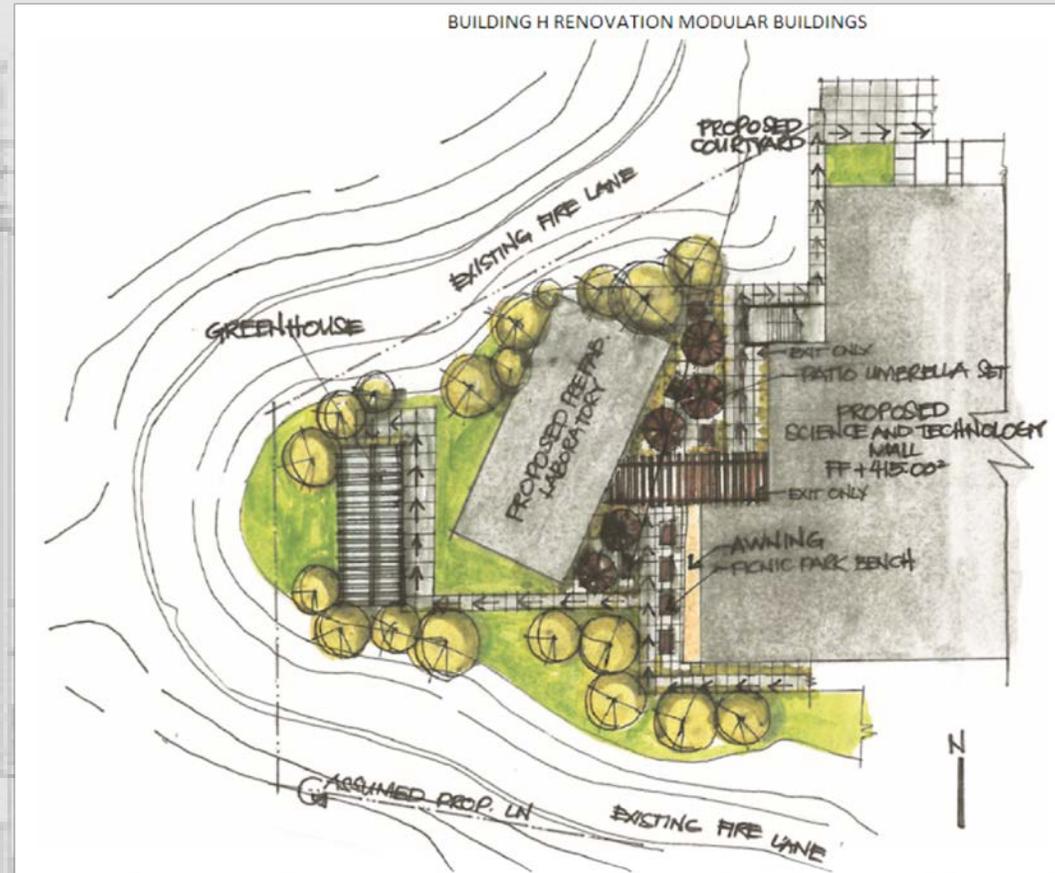

Central Plant & Year 5 Energy Upgrades

Funding:

- Prop V, Prop 39 & SDG&E

Design:

- Complete

DSA Submittal

- Approved

Bidding/Award:


- Bid opening-March 4th

Construction:

- May 2019-May 2020

Status:

- Temporary chillers to be installed on Building E planter area
- Sound walls to be erected adjacent to building E

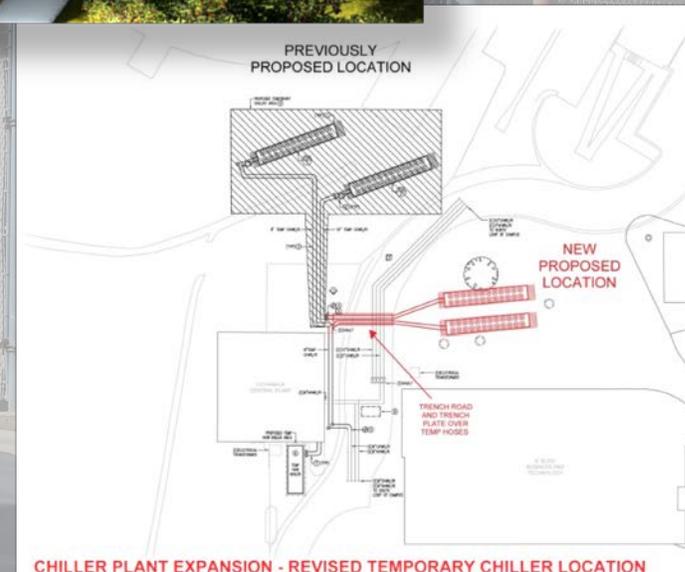

Campus Facilities Project – Campus Improvements Phase II

Funding:

- Fund 41

Scope:

- Covered cart parking with charging on N side of Bldg C
- Exterior shade structure for south windows of Bldg A
- Relocate bollards north of LRC
- CDC casework modifications
- Install bollards at fire hydrants, PIVs & backflows
- Replace backflow valves on domestic and fire lines
- Campus wide signage

Design:

- In development / Will require DSA approval
- RFP for Fire Systems assessment released on February 8

Bidding/Award:

- TBD

Construction:

- TBD



Learning Resource Center Reroof Project

Funding:

- Scheduled Maintenance

Design:

- February 2019 to March 2019

Bidding & Award:

- March 2019 to May 2019

Construction:

- Summer 2019

Status:

- Architectural design firm selection process



CDC Shade Structure

Funding:

- CDC Grant

Scope:

- Install new shade structure at playground

Design:

- Complete

DSA:


- February 15, 2019

Bidding/Award:

- February 2019

Construction:

- May 2019

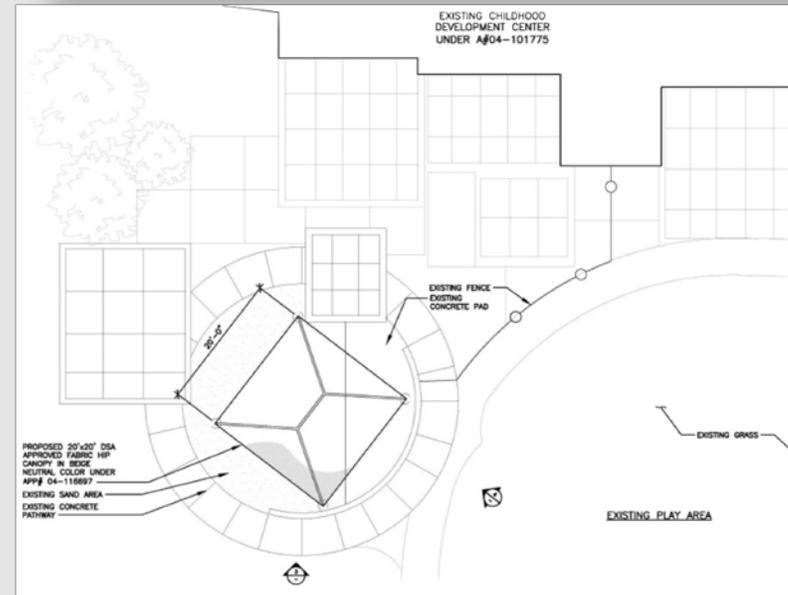

FOSY Fencing

Funding:

- Fund 41

Scope:

- Install new steel fencing and gates

Design:


- Complete

Bidding/Award:

- February 2019

Construction:

- April 2019

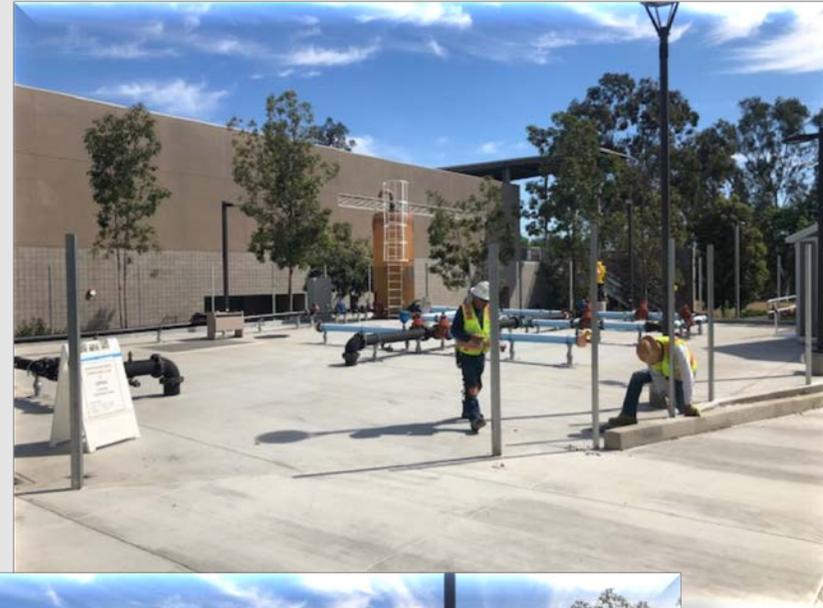

Questions

